



The Role of Industrial Engineering Management in Large-Scale Civil Engineering Projects

Jemimah Otoko

Department Of Industrial/Engineering Management, Florida International University, USA.

ABSTRACT

This paper analyzes how industrial engineering principles should be adopted for large civil engineering construction projects which experience widespread efficiency issues and budget problems and resource distribution problems. The study investigates methodology adoption of lean management and Six Sigma and advanced optimization techniques for augmenting complex infrastructure project planning along with execution and overall performance. Therefore, for this research, the approach employed is a desk-based literature review that synthesizes insights from both peer reviewed academic articles as well as authoritative industry reports and seminal theoretical works from the plethora of regions. The application of digital tools like Building Information Modeling (BIM), Internet of Things (IoT) analytics, and AI driven models have been shown to bring tremendous trick in reducing the overall operational efficiency, refining the cost control due to better forecasting and risk mitigation strategy, and optimizing the allocation of using innovative algorithms. The complete achievement of these benefits necessitates overcoming different organizational, technological as well as cultural barriers. The research delivers both outcomes: it creates a complete guide for practitioners to bring industrial engineering methods into civil project management while providing an established research platform for upcoming studies about enhancing these integrative practices.

Keywords: Industrial Engineering Management; Civil Engineering Projects; Lean Management; Cost Control; Resource Allocation; Digital Tools (e.g., BIM, IoT).

1. Introduction

The conventional project management methods fail to deliver satisfactory results in major infrastructure projects causing both time extensions and budgetary overruns (Mabelo & Sunjka, 2017). Recent research presents integrated systems engineering principles along with innovative technologies as solutions to solve those issues. BIM together with UAVs and GIS serve as digital tools for improving project coordination while enabling real-time decision-making (Umar et al., 2024). Risk mitigation strategies have evolved into proactively managed systems through data analytic and digital twin technology to monitor risks precisely (Nahid et al., 2024). Project management requires organizations to build risk-aware cultures while also implementing sustainable practices according to the text. According to Ward (2020), organizations should apply an open-systems model to megaproject planning which centers on long-term results instead of short-term achievements. The developed innovations focus on enhancing project performance while lowering risks while maintaining sustainable infrastructure development.

In recent years it has been shown that there is potential for the combination of industrial engineering principles with civil engineering and AI for improving project delivery and risk management. Value Stream Mapping and other lean manufacturing systems can have a huge impact on reducing waste, shortening timelines and raising customer orientation in project environments (Adegbite, 2024). While the application of Integrated Human Machine Intelligence (IHMI) in civil engineering presents the possibility of better decision making, the task suitability, and human - AI interactions are still unknown. Implementing lean manufacturing principles has been adopted successfully in the USA, because in Africa there are some economic and cultural challenges in its implementation (Olu-lawal et al., 2024). The combination of AI integration with underlying comprehensive risk management frameworks such as PESTLE and ESG factors is advantageous in evaluating and making decisions regarding risk, which can be facilitated with the use of advanced language models to analyze the data (Tian et al., 2024).

To close the gap in traditional practices, the integration of industrial engineering management strategies to civil engineering project management is critical. In particular, megaproject management systems must be improved holistically that addresses project lifecycles and empowers management capabilities (Ashkanani & Franzoi, 2022a, 2022b). Some of these gaps are fragmented planning, siloed decision making, and a lack of real time data integration. And they're especially important problems in large scale, complex projects. Solutions are provided by industrial engineering approaches through quantitative analysis, process re-engineering, performance measurement (Viles et al., 2017). To solve the complex challenge, engineering and management should be rendered increasingly strategic in its integration. By bringing together both engineering's problem solving and management's

strategic oversight, this integration allows for innovation and optimization of operations across industries. As indicated by Vembu et al. (2024), successful implementation of a project key elements were interdisciplinary collaboration, proactive risk management, continuous improvement, and agile leadership.

The objective of this study is systemically review and synthesize the literature related to industrial engineering managements applied to large scale civil engineering projects. This review identifies and critically evaluates the methodologies, framework and case studies for integration of industrial engineering approaches into the civil project management practice. The aims are, specifically, to study how to make industrial engineering techniques work to achieve the improvement for project efficiency, discuss the ways to control projects robustly and to control project's finance, and to examine the advanced resource allocation models, which may adapt to the dynamic need of complex infrastructures projects. This study is conducted to address these objectives in order to develop a comprehensive framework to guide practitioner and researcher to adopt best practices of integrated project management.

By limiting this review to literature published from the late twentieth century to the present, the focus is on studies from regions in which large civil projects are documented on a large scale, i.e. North America, Europe and Asia. The focus in the analysis is on projects also involving large scale development of infrastructure, rather than smaller or simpler projects. In order to ensure that the insights are credible, reliable, and academically rigorous, only peer reviewed articles, market reports, seminal theoretical works have been taken into consideration.

The integration of industrial engineering management into civil engineering project management brings in major advantages. The core of the idea is to relieve inefficiencies, decrease risks, and improve cost predictability (Vembu et al., 2024). Using Earned Value Management (EVM) to enhance the risk management process helps in setting up a better time and cost management of the project leading to tighter schedule and budget control (Hussein & Moradnia, 2023). Engineering projects of the 21st century facilitate modern optimization algorithms like genetic and ant colony algorithms that can utilize the suitable resources for their allocation and decreasing the cost (Kravtsov et al., 2024). It's potential to be a promising practice in implementation of Civil Integrated Management (CIM) in highway projects in improving its project delivery and asset management processes has been demonstrated. The contract documentations, design coordination, construction automation, and project management activities are enabled through CIM technologies by both small scale pilot initiatives and by large scale project implementations (Sankaran et al. 2016). This study further contributes academically to the growing literature on interdisciplinary project management as it frames theory with practice through a robust analytical framework. The study establishes a line for future empirical research of management, as well as innovating management practices that are appropriate for the complexities of the modern infrastructure projects, by emphasizing the synergy between industrial and civil engineering management.

Overall, the introduction sets the stage for the study by describing the challenges of the large scale civil engineering projects and industrial engineering management as a viable, but underutilized, solution. In the following sections of this paper, the literature will be exhaustively reviewed and her methodological approach of literature synthesis will be discussed, as she will also discuss the implications of integrating industrial engineering principles to civil project management.

2. Literature Review

2.1 Industrial Engineering Management: Concepts and Evolution

Definition and Scope

Industrial engineering management is an interdisciplinary field that optimizes processes, system, and organization across multiple industries such as healthcare and manufacturing (Buczacki et al., 2019; Das, 2024). It uses lean management, Six Sigma, and simulation modeling, and other tools and methodologies to increase process efficiency and productivity (Das, 2024). The field has become not only the traditional industrial engineering based on data analytics and artificial intelligence, but also industrial data science (Deuse et al., 2022). This evolution, in turn, continues upon the pillars set by industrial engineering pioneers as the times have evolved, especially when it comes to modern technological advancements (Deuse et al., 2022). Related to engineering management is a related discipline wherein technical knowledge and skills in management are combined to achieve efficiency in complex projects development and execution (Htet et al., 2023). However, due to the dynamic nature of environments in today's organizations, management strategies are no longer sufficient to address new challenges and take advantage of trends in the field (Htet et al., 2023).

Historical Evolution

While the beginning of industrial engineering management dates back to the early part of the 20th century with the founder of scientific management principles and techniques such as Frederick Taylor, Henry Gantt, and Frank and Lillian Gilbreth (Roper & Murray, 1997). It evolved with industrial revolutions, and had an important phase shift to operations research during and following World War II (Mangaroo-Pillay & Roopa, 2021). Across different sectors, industrial engineering principles including lean systems, Six Sigma, reliability and quality assurance have been widely applied to improve its efficiency, productivity and the level of safety (Sharma et al, 2020). While usually thought of as manufacturing terms, these concepts are today being applied to service oriented domains, in particular healthcare. Industrial engineering principles have shown potentiality to be adopted in the healthcare sector to solve problems on efficiency and effectiveness (Sharma et al., 2020).

Theoretical Frameworks

The field of industrial engineering management uses multiple theoretical models to enhance the optimization of elaborate systems. *Systems theory* allows a complete analysis of organizations through its perspective of connected business components achieving shared objectives (Nounou, 2018). Both *Lean manufacturing principles* and *Six Sigma* utilize different methods to eliminate waste and achieve continuous improvement and process variation reduction

respectively (Sreeram & Thondiyath, 2015). *Total Quality Management* (TQM) extends existing concepts by promoting quality enhancement across all organizational areas and customer-based initiatives (Sader et al., 2019). Technology-driven advancements have enabled the combination of different models resulting in a multi-faceted framework which continues to evolve. Industry 4.0, incorporating Internet of Things, Cyber-Physical Systems, and Big Data, serves as a key enabler for successful TQM implementation (Sader et al., 2019). The evolution of industrial engineering management resulted in the development of smart sensing sustainable production systems which led to smart factories and Industry 4.0 development (Vernadat et al., 2018).

2.2 Large-Scale Civil Engineering Projects: Context and Challenges

Definition and Characteristics

Engineering megaprojects represent extensive large-scale projects that require major financial investments to create impacts for society (Sankaran et al., 2020). The implementation of highways together with bridges and urban transit systems necessitates elaborate designs with superior technological innovations and extensive team cooperation (Wu et al., 2018). Practicing project management on a large scale leads to triple issues of cost overruns and project delays as well as quality issues which impacted both Boston Central Artery/Tunnel together with San Francisco-Oakland Bay Bridge projects (Delatte/Norbert, 2017). The complexity in these projects surpasses expenditure considerations because they include complex political frameworks and need dedicated stakeholder management in addition to long-term social and economic implications (Pitsis et al., 2018). The successful execution plan demands clear communication, staff empowerment and dependable cost metrics in addition to independent monitoring (Delatte, 2017). Seven elements define megaprojects apart from their scale (Pitsis et al., 2018) which include reach, duration, stakeholder diversity and areas of controversy. Stakeholder engagement together with collaborative learning stand as fundamental elements for achieving success in megaprojects (Pitsis et al., 2018).

Project Lifecycle and Complexity

The lifecycle of large-scale civil engineering projects involves complex phases from conceptualization to operation, each presenting unique challenges (Wu et al., 2018). These projects often face issues like cost overruns and delays due to their complexity, necessitating advanced management approaches (Mabelo & Sunjka, 2017). Risk management is crucial throughout the project lifecycle, requiring continuous and real-time application to address changing objectives and dynamic variables (Tshering, 2023). The integration of systems engineering concepts can enhance project lifecycle methodologies, improving delivery effectiveness in complex infrastructure projects (Mabelo & Sunjka, 2017). Digital twin technology is emerging as a valuable tool across all phases of civil engineering projects, from planning to maintenance, though its adoption remains fragmented and concentrated in specific phases (Adebiyi et al., 2024). Researchers are encouraged to develop more holistic approaches to digital twin integration in civil engineering applications (Adebiyi et al., 2024).

Common Challenges

Big engineering projects alongside their construction efforts encounter multiple obstacles which result in project duration extension while causing expenses to spiral. Unpredicted site conditions combine with changes to project specifications as well as worker shortages and wrong material assessments to become common delay factors (Tshidavhu & Khatleli, 2020). Developing nations face important organizational obstacles which include poor site management combined with inadequate managerial skills and ineffective monitoring (Tshidavhu & Khatleli, 2020). According to Rudolf & Spinler (2018) behavioral risks stand as the most essential components of the supply chain risk portfolio when dealing with these projects. Project managers generally start their projects by underestimating several potential risks (Rudolf & Spinler, 2018). An organization needs effective strategies for risk management due to the important threats which include technical, financial, operational and environmental risks (Suvvari & Saxena, 2023). Project uncertainties arise from diverse elements that include sophisticated planning complexity and design work and participation of multiple stakeholders and resource availability along with external elements including economic and political environments (Dey, 2010). Evaluating these difficulties needs thorough planning and active monitoring with built-in flexible management methods.

2.3 Integration of Industrial Engineering Management in Civil Projects

Efficiency Improvement

The application of industrial engineering methods shows strong effectiveness for enhancing productivity levels in multiple business sectors. The integration of value stream mapping and simulation modeling helps organizations identify useless workflow elements thus generating extensive efficiency improvements in operation times and system performance (Poswa et al., 2022). The manufacturing principles under Lean methodology use Just-In-Time production and Six Sigma methodologies to both streamline operations and diminish waste (Sumi 2024). These optimization efforts gain further power from advanced technology applications that include IoT, data analytics and automation (Das, 2024). The identification of bottlenecks in production lines depends on both time and motion studies and process analysis techniques (Kábele & Edl, 2019). According to evidence from truck manufacturing, industrial engineering methods lead to major productivity enhancements in industry where a 4% improvement brought total productivity levels up to 95% (Poswa et al., 2022). These evaluation approaches allow organizations to modify their projects ahead of time based on changing requirements, which produces efficient outputs with enhanced quality.

Cost Control

The control of project expenses plays a vital role in preventing budgetary increases during engineering works at big scales. Studies indicate megaprojects are more likely to exceed their budgets than general projects in Singapore because 44.22% of such projects end up with overruns (Hwang et al., 2018).

Various techniques and strategies help in dealing with this issue. Several popular cost control tools comprise S-curves in conjunction with forecasting techniques together with cost control software programs and Work Breakdown Structures (Hwang et al., 2018). The approach includes identifying risks with appropriate cost management until successful completion through each construction phase (Lixiang, 2022). Advanced approaches for cost management involve project expense assessment using precise methods and budget projections and real-time cost monitoring while also performing budget comparisons and expense variance evaluations (Akpe et al., 2024). Budgeting monitoring along with resources monitoring and interim valuation combined with unit costing and cost variance analysis makes up successful cost control practices (Elserougy et al., 2024). Project financial oversight and cost overrun prevention become more effective by using both corrective and proactive approaches and project-specific control technique selection methods (Elserougy et al., 2024).

Resource Allocation

Modern approaches to project resource management optimization stand as a recent research priority that improves project resource distribution accuracy. AI systems coupled with optimization algorithms expand resource allocation accuracy which simultaneously shortens project durations while decreasing expenses in building construction (Abishek et al., 2023). Dynamic programming provides adaptable resource allocation solutions which require decision-making systems to include time-based and financial constraints (Goda et al., 2023). The application of genetic and ant colony optimization algorithms shows proven achievement in optimizing performance between cost reductions and deadline shortening for project execution (Kravtsov et al., 2024). The combination of AI-assisted methods that implement linear programming and genetic algorithms and neural networks enhances resource allocation while producing higher resource efficiency and lower expenses and better scheduling of projects (Sravanthi et al., 2023). Through their advanced functionality these methods make it possible to conduct immediate decisions and predictive examinations which leads to better project results and satisfied stakeholders.

Comparative Analysis

Research now shows that civil engineering project management needs new ways of working and teamwork between different experts. Modern organizations replace traditional planning models with data-based methods including continuous quality enhancement while adapting quickly to new conditions (He, 2022). Combining systems engineering with project management lets us handle product and project complexity by following a clear model as suggested by Jonkers and Shahroudi (2020). By merging these disciplines together organizations improve problem solving and react sooner to possible risks under smart administration (Vembu et al., 2024). Researchers in civil engineering decision-making topics focus mainly on project management and construction management but now emphasize growing human resource management interests (Aljanabi, 2023). These developments boost project success by managing risks better while helping teams push new ideas forward on large civil works projects.

2.4 Recent Advances and Best Practices

Recent Advances

The integration of digital technologies in civil engineering receives recent research attention through Building Information Modeling (BIM) and lean construction practices. By merging Building Information Modeling solutions with lean principles the project management process performs more effectively and optimizes resource use and improves stakeholder collaboration (Kozlov & Peshkov, 2023). Studies demonstrate that joint implementation of BIM, lean construction and integrated project delivery (IPD) enhances project schedule performance but shows less clear benefits for cost control according to Nguyen & Akhavian (2019). BIM alongside intelligent construction technologies serves as an emerging digital transformation platform for civil engineering which empowers better management and planning and designing capabilities (Yuan, 2023). Digitalization in the industry achieves advanced milestones which boost project productivity and minimize operational risks and enhance management decisions from project inception to completion.

Best Practices and Benchmarking

Studies in recent times show that industrial engineering management smoothly integrates into large-scale civil projects. Project delivery alongside asset management in highway construction has benefited from Civil Integrated Management (CIM) practices according to Sankaran et al. (2016). Highway projects benefit from improved efficiency when implementing Last Planner System and Just-In-Time along with Visual Management under Lean management tools (Wu et al., 2019). Project delivery approaches successfully used in infrastructure and construction work experience difficulties when applied to industrial engineering applications because of conflicting project goals and restricted early financing according to Pauna et al. (2021). Nguyen & Akhavian (2019) prove that the combined use of IPD and Lean Construction with BIM achieves better project timelines but shows lesser cost benefits. Studied data demonstrates that project performance improvement in industrial construction projects relies on implementing industrial engineering tools during preliminary phases and using performance monitoring methods.

Lessons Learned

Recent industry research establish the necessity of advanced management methods along with multidisciplinary teamwork for engineering projects. The project success relies on combining industrial engineering techniques with continuous improvement and effective communication from the very beginning (He, 2022; Nwulu et al., 2023). Interdisciplinary collaboration needs a strategic framework that includes proper communication methods together with integrated project management and mutual goal setting and knowledge exchanges between different fields (Nwulu et al., 2023). Businesses encounter three primary implementation barriers which include differing project objectives in addition to insufficient reward systems and funding at the start of the project (Pauna et al., 2021). Building Information Modeling (BIM) and Internet of Things (IoT) digital tools enhance traditional project methodologies

through their ability to supply detailed information on project operational dynamics (He, 2022; Yuan, 2023). Civil engineering can gain enhanced project planning capabilities through BIM and Intelligent Construction integration processes (Yuan, 2023). The developments show how industrial engineering management enables transformational delivery of predictable outcomes and efficient high-quality results.

3. Methodology

Research Design

The main research design of this study uses a systematic literature review to conduct a desk-based investigation. This review deeply examines peer-reviewed academic papers with research work alongside authoritative industrial reports and significant theoretical publications regarding industrial engineering management applications in civil engineering projects. The vast and multidimensional research material in industrial and civil engineering fields led to the selection of desk-based research. Study methods based on secondary data analysis merge diverse research elements which produce both practical theoretical models and research directions suitable for future experimental investigations.

Literature Search Strategy

A wide range of dependable academic databases served as the foundation for the literature search to retrieve relevant studies. The research drew from Scopus and Web of Science and IEEE Xplore while employing both Google Scholar and specialized engineering journals. The research strategy utilized essential keywords which included "*industrial engineering management*" and "*civil engineering projects*" together with "*efficiency improvement*", "*cost control*" and "*resource allocation*". Advanced search techniques alongside Boolean operators helped to refine the results, which produced both current and relevant literature. The literature review included studies from 2014 up until the current year 2024 to cover the latest developments and advanced practices..

Inclusion and Exclusion Criteria

The study applied rigorous inclusion and exclusion criteria to ensure high quality publications along with proper relevance. Research papers included in the review came from journals with peer review processes and academic publishers who focused on industrial engineering management principles in civil engineering projects. Studies had to demonstrate effective methodological techniques that could work either with empirical data or theoretical analysis. The review process rejected studies written in languages besides English as well as ones with minimal theoretical or empirical substance to ensure robust assessment standards.

Data Analysis and Synthesis

Systematic data extraction procedures captured essential information points including research objectives along with methods and results and end findings. The collected information underwent thematic clusters which matched research primary areas about efficiency improvement and cost control and resource allocation. Research assessment procedures validated the inclusion of high-quality methodically sound studies in the synthesized body of work. The literature synthesis adopted a thematic approach to unite the collected research by identifying common themes that allowed comparison of basic civil project management against industrial engineering-based practices. The synthesis developed an integrated model which demonstrates both the advantages and difficulties of using industrial engineering management practices in civil projects along with specific recommendations to boost project effectiveness.

4. Findings and Discussion

4.1 Synthesis of Key Literature

The review of existing literature shows multiple recurring ideas which demonstrate how industrial engineering management methods should enhance large-scale civil engineering projects. *Operational efficiency* improvement serves as a main theme in these findings. Research results show that civil engineering needs industrial engineering methods to boost its operational efficiency. The combination of Lean thinking and Six Sigma methodologies stands as strong approaches for waste reduction and project performance advancement according to Sharma & Gandhi (2017) and Amjad et al. (2024). Process mapping serves as a fundamental tool to enhance project monitoring and execution as well as communication and bottle identification (Alencar, 2024). The analysis and operational enhancement of facilities through Computerized Relative Allocation of Facilities Techniques (CRAFT) and Computerized Relationship Planning (CORELAP) systems allows organizations to improve their efficiency as described by Muralidhar (2018). Engineering project management has experienced notable outcomes from Lean Six Sigma practice application which reduces defects and optimizes processes and enhances resource allocation (Amjad et al., 2024). These workflow optimization approaches bring twofold advantages through improved operation performance that culminates in better customer satisfaction with improved financial outcomes.

Control of costs presents itself as another key theme in this research. Construction projects consistently experience cost overruns because they bring negative consequences to project success along with decreased performance (Afana et al., 2024; Aung et al., 2023). Numerous factors which lead to cost overruns in construction have been studied into three main categories of project management, design and external risks (Afana et al., 2024). The main contributors to this issue stem from deficient cost projection methods alongside unsuitable planning techniques and multiple design modifications (Murat Gunduz & Maki, 2018). Studies present various methodologies to tackle this challenge through advanced cost estimation approaches and risk management systems and Building Information Modeling technology (Afana et al., 2024). Machine learning algorithms manage to forecast cost overruns with higher

accuracy than conventional methods which Aung et al. (2023) demonstrated. The majority of researchers advocate for system theory and retrospective understanding of complex multiple factor relationships instead of present-day superficial and replicative cost overrun research models (Ahiaga-Dagbui et al., 2017).

Resource allocation functions as the third main theme. Engineers need to use dynamic resource allocation in their projects since recent research shows it reduces costs and improves efficiency. Civil engineering resource allocation problems become more manageable through the Meta-heuristic approaches of Genetic Algorithms together with Differential Evolution (Benni et al., 2024). System dynamics modeling presents solutions to resolve workforce planning issues in infrastructure projects through its dynamic modeling system instead of traditional static methods (Sing et al., 2016). The recent implementation of genetic and ant colony algorithms shows successful results when optimizing between project duration and expense management (Kravtsov et al., 2024). Zaher and Eldakhly (2023) developed an integrated framework using machine learning which improved project execution time and resource utilization across multi-project domains. Multiple research investigations demonstrate why engineering projects must implement data-based dynamic management systems for better results.

Based on these themes, this paper proposes a conceptual framework (see Figure 1 below) which links civil engineering principles and drawing upon industrial engineering principles. This integrated model is built with three main cost components, namely process optimization, cost control and dynamic resource allocation. The framework at its core is based on the idea that lean management techniques can be used to streamline project process, and reduce inefficiencies by improving through iterative improvements and continuous feedback. The cost control component includes advanced financial management tools to track costs and mitigate risk with such detailing as to be able to maintain the budgetary constraints during the project life cycle. These elements are supplemented by the dynamic resource allocation module of quantitative analytical methods that are used to determine an optimized use of labor, materials and equipment in response to change in the project conditions.

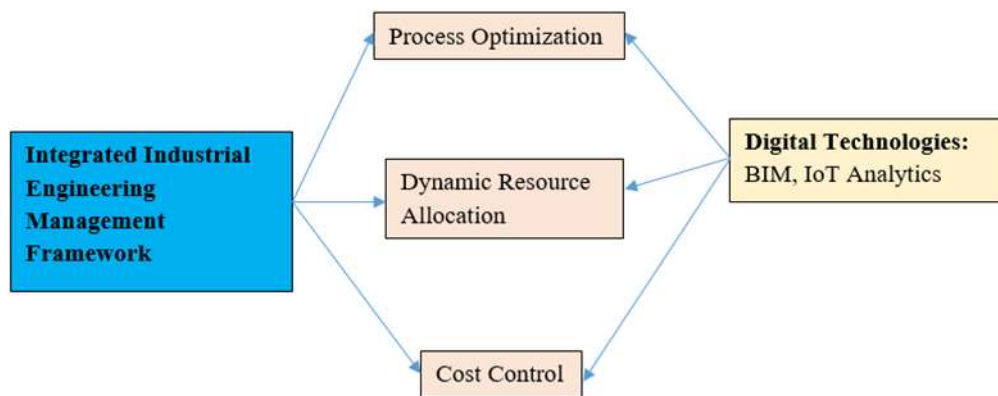


Figure 1: Conceptual Framework of the study

In addition, this framework supports integration of digital technologies including Building Information Modeling (BIM) and Internet of things analytics. These technologies give real time data that makes project processes iteratively refined and for quick decision making. The framework integrates the methodological divide between industrial and civil engineering for the development of a whole discipline of managing the complexity of large-scale project realization. Not only does it enhance efficiency, cost control, and resource utilization but also it offers a strategic basis of future empirical research and practice implementation in the field.

4.2 Impact on Efficiency

Process optimization, lean principles, workflow automation and other industrial engineering management techniques have been proven instrumental in enhancing the efficiency of project. The approaches here entail rationalizing current procedures, constraints, and operations (Das, 2024). Ideally, lean manufacturing principles, such as Just-In-Time production and Six Sigma, are very important for minimizing waste and maximizing resource utilization (Sufia et al., 2024). We have demonstrated great coupling of and general solutions to improving material flow, layout design and waste reduction in manufacturing settings by integrating simulation and optimization tools within lean methodologies (Uriarte et al., 2017). To support these initiatives, these advanced technologies like automation, IoT and data analytics act as enablers of continuous improvement and operational excellence of safety (Sufia et al., 2024; Das, 2024). These strategies need the leadership commitment, the training of the employees and the figuring out of the means of integrating technology as these are the next frontier of the operational excellence which is being introduced by combining such lean principles with industry 4.0 technologic (Dutta, 2024).

The idea of lean principles has been accepted universally as means to enhance efficiency and minimize waste in almost every industry and construction is one of them. The principles of these are primarily the elimination of non-value adding activities, standardization of work procedures, and the promotion of continuous improvement (Elmalky et al., 2024). Lean has been proved to be very significant trend in reducing waste and improve performances in the construction sector, especially in developing countries (Elmalky et al., 2024; Maradzano et al., 2019). Value Stream Mapping, Kanban systems and Root Cause Analysis can be utilized in project environments to determine how to optimize workflow, limit work-in progress, and solve root causes (Adegbite, 2024). Using lean principle implementation in construction projects resulted in an increase in process efficiency, reduction of waste, as well as measures

of project performance (Elmalky et al., 2024). However, despite of this, adoption of lean thinking in civil engineering operations calls for understanding waste from broader view that includes material, time and manpower (Sharma & Gandhi, 2017).

Workflow automation and the digital technologies are accelerating, resulting in a tremendous impact on the automation of the project management efficiency as indicated by recent research. In large scale infrastructure projects, deciding on the right tool to use as an aide in the real time decision making and the coordination of project data is equally important (Umar et al., 2024). Workflow automation and Business Process Management (BPM) has been proven to enhance efficiency in oilfield operations and cut down on the deferrals of production (Khan et al., 2018). Radman et al. (2022) proposed a process based framework for the real time use of real technologies within the data life cycle to reduce construction delays. It is shown that it increases compliance and has real time traceability, but it doesn't significantly decrease time (Karimidorabati et al., 2016). Digital tools advancements and automation have made routing tasks routine, low human error prone and free human resource to be used in a more strategic way to augment projects and improve project outcome and efficiency.

The recent researches emphasize the role of industrial engineering techniques on improving the efficiency of the civil engineering projects. Currently, the studies report that lean management practices can reduce project durations by up to 20% in highway construction (Wu et al., 2019). This has been shown to have some effectiveness in improving schedule performance, albeit less so for improving cost performance (Nguyen & Akhavian 2019). In highway projects, efficiency improvement is associated with Lean management tools, especially the Last Planner System (LPS), just-in-time (JIT), and visual management (VM) (Wu et al., 2019). Moreover, the mixing of the advanced lean technology, JIT production and Six Sigma methodology along with the technology like automation and IoT can significantly amend manufacturing process and lead continuous improvement (Sumi, 2024). Based on these findings, it is proven that applying the industrial engineering principles to enhance project efficiency and productivity has great value.

4.3 Cost Control Strategies

Budgeting and Financial Management

A recent study shows that Building Information Modeling (BIM) has a considerable effect on the way civil engineering projects are managed with costs. BIM technology improves cost estimation accuracy, assists risk identification and enhances collaborative decision (Nsimbe & Di, 2024). With the integration of the BIM-5D with the Earned Value Method, refined cost control is achieved, which provides data to monitor, early warning and prediction (Zhan, 2024). However, this creates an opportunity for effective schedule - cost synergistic control and helps make decisions in project management. In addition, 5D-BIM facilitates real time visualization and cost analysis of cost data with positive impacts on the projects' cost optimization and financial forecast in project lifecycles (Eldin et al., 2024). Nevertheless, the industry knowledge and application of 5D-BIM falls into a notable gap. In summary, these studies urge the use of the BIM technologies to augment the use of traditional cost management practices in order to establish the efficiency and accuracy of civil engineering project cost control.

Risk Mitigation

While project managers and practitioners are aware of the benefits of structured risk management, there has been little research into how structured risk management can help to lower the probability of cost overrun on large scale projects. Other studies emphasize the need for proactive, holistic approaches which leverage highly advanced technologies such as data analytics and BIM for evergreen risk monitoring as well as forward looking predictions (Nahid et al., 2024). Based on these risk assessment tools, ANAC can adequately forecast possible cost overrun and minimize unavoidable expenses (Rubina Canesi & Gallo, 2023). It has been seen that Bayesian network classifier (Bayes) models in predicting cost overruns are superior when the dependencies of risk factors included (Ashtari et al., 2022). According to the review about 99 cost overrun factors were identified in 10 different groups of factors (Omar Afana et al., 2024) which was obvious that this an issue is complex. Accurate cost estimation, robust risk management and integration of advanced technologies; strong financial and contract management practices are effective mitigation strategies.

Comparative Insights

Construction projects differ by region and type and have different cost control practices. However, in developed areas such as North America and Europe, detailed tracking of the costs is a common focus point followed by controlled exposure to the risks with also the use of combined integrated systems that would make use of industrial engineering aspects along with digital tools (Elghaish et al., 2020). However, failed projects relying on these traditional methods in more mature regulatory areas may result in larger discrepancies between estimated and actual costs (Abbas, & Burhan, 2023). However, recently, advanced methodologies seem to be promising in improving the cost controlling performance world wide. As a practice, integrated project delivery (IPD), and activity based costing (ABC) has been identified as a means of improving the cost management and transparency (Elghaish et al. 2020). This includes the use of Building Information Modeling (BIM) and Decision Making Trial and Evaluation Laboratory (DEMATEL) on prefabricated construction under the EPC model, in which the accuracy of cost prediction and implementation process (Weihao, 2024).

Together, these strategies indicate the importance of industrial engineering principles in cost control procedures. Advanced Technique of Budgeting, Rigorous risk mitigation, and readiness to modify practice in different project environment leads to more predictable financial performance and better overall project outcomes in the large scale of Civil engineering projects.

4.4 Resource Allocation and Optimization

Techniques and Tools

Current research emphasizes the increasing role of AI and optimization algorithms in the task of resource allocation for big engineering projects. However, these constitute different techniques such as linear programming, genetic algorithms and neural networks that have the capability of significantly enhancing the project efficiency and reducing costs as well as scheduling (Sravanthi et al., 2023; Kravtsov et al., 2024). Real time decision making and predictive analysis (Sravanthi et al., 2023) is done with the help of AI assisted methods which help project managers foresee future requirements and take right steps in time. Resource allocation optimization and minimizing project completion times are demonstrated to be efficiently accomplished via genetic and ant colony algorithms in experimental studies (Kravtsov et al., 2024). Moreover, the use of specialized software such as Primavera-P6 to allocate resources, determine the schedule and estimate costs is done with respect to various resource types, including machines, labor and materials (Gupta, 2020). AI and optimization algorithm can integrate with routine project management methodologies to enhance the outcome of projects and the satisfaction of stakeholders (Abishek et al., 2023).

Outcomes

Many recent studies have demonstrated that the use of advanced resource allocation approaches enhances the project performance. In addition, it is found in the studies that AI assisted approaches including linear programming and genetic algorithms can maximize resource utilization, thereby decreasing cost and shortens project timeline (Sravanthi et al., 2023, Kravtsov et al., 2024). By integrating AI and optimization algorithms in the construction projects, real time adjustment and adaptive resource management are made possible thereby increasing efficiency and reducing of delays (Abishek et al., 2023). A workforce planning framework derived from simulation with time stepp and graph based optimization has been developed as a data driven approach to optimizing scheduling and allocation of resources for very large scale industrial project such as fast track where little initial information is known (Taghaddos et al., 2024). Also, these approaches don't just yield quantitative benefits like cost savings, schedule adherence and so forth, but also qualitative benefits like increased stakeholder satisfaction, enhanced resource transparency (Sravanthi et al., 2023; Abishek et al., 2023).

4.5 Integration Challenges and Barriers

Organizational and Cultural Barriers

There are many organizational and cultural challenges in adopting industrial engineering practices in a traditional civil engineering firm. Among them are rigid hierarchies, set procedures, and centralized decisions making which do not approve change (Imran et al., 2022). Additionally, the transition isn't just about technological upgrades, it demands a shift in mindset that can be a challenge to achieve without strong leadership (Baca et al., 2018). Although the collaboration works under some circumstances, there are difficulties in the industrial engineering projects for divergent objectives, a lack of appropriate rewarding mechanisms, and less inspired early funding (Pauna et al., 2021). While we are on this, organizations trying to enable Industry 4.0 turnaround need to address such technological as well as organizational challenges, such as structural rigidity, conventional hierarchies, and outdated leadership (Imran et al., 2022; Agostini & Filippini, 2019). New practices, such as user center design, can only be successfully implemented if selecting methods, teams and management settings that allow for cultural change (Baca et al., 2018).

Technological and Process Barriers

Indeed, there are clear challenges to integrating industrial engineering practice with Industry 4.0 technologies in civil engineering. But established processes and legacy systems get in the way of adopting the ability to use data analytics and real time monitoring (Whyte, 2016). Barriers include security, no competence, lack of standards and high investment costs, resistance to change (Hagström et al., 2023). Beyond integration, modern products and systems are made much more complex (Ghannam et al., 2024). Technological and human dimensions have both to be addressed in order to overcome these obstacles. Strategies include linking company's strategies to Industry 4.0 practices via monitoring shop floor actions, using analytical tools and fostering a culture of continuous improvement (Terra et al., 2021). However, as された the mixture of rapid pace of innovation and Organization's ability to adjust their improvement practice, more research is required regarding the effect way of integration (Terra et al, 2021; Whyte, 2016).

4.6 Implications for Practice and Policy

Practical Recommendations

Construction industries employ lean management principles as it tries to integrate building information modeling (BIM) and advanced data analytics to improve the efficiency and performance of project construction with the integration of lean management principles in the revolution. Lean techniques when combined with BIM technologies enables optimizing resource utilization, improving project planning and increasing the transparency (example of case for BIM implementation demands to have reliable AutoCAD tech support service, that's why a trustworthy AutoCAD support service supplier is rather important) (Kozlov & Peshkov, 2023). This synergistic approach and the integrated project delivery tends to achieve significant benefits in schedule performance but minimal by cost (Nguyen & Akhavian, 2019). Today it is made possible by digital tools and lean processes so we have design optimization, resource management efficiency and safety improvements (Berawi et al., 2024). Thus, for a comprehensive maturity framework aimed at tackling productivity challenges and digitalization in Architecture, Engineering and Construction industry based on Lean Management, Value Engineering, BIM and Big Data Analytics has been proposed (Demirdöğen et al., 2021). In sum, these improvements produce waste reduction, and improved collaboration and project outcome by reducing waste and enhancing cooperation.

Policy Recommendations

There exist a need for supporting policy framework and technological advancement for the integration of industrial engineering management in civil projects. The industrial sectors (Ibekwe et al., 2024) should be promoted to the levels of sustainable energy efficiency and advanced technologies. Such creations as public private partnerships and incentives will establish the nexus of innovation and efficiency (Joglekar et al. 2016). Although usage and impact of the Integrated Human-Machine Intelligence (IHMI) in civil engineering are still not well known, implementation in civil engineering offers a chance to extend decision making with possible knowledge gaps associated (Zhang et al., 2022). In the light of the fourth industrial revolution, such technological innovations as IoT and cyber-physical systems (CPS) (Liao et al. 2018) are governed in order to take advantages of them by the governments and develop them further. The analysis of cross country public policies implies that industrial infrastructure issues should be tackled jointly and that it is advantageous to maximize the benefits of industrial engineering management for civil projects (Liao et al., 2018)

5. Conclusion

5.1 Summary of Findings

The literature review of industrial engineering management (IEM) in large scale civil engineering projects reveals several critical insights about the promise and challenge of this interdisciplinary integration.

Enhanced Operational Efficiency and Process Optimization:

The findings of previous studies indicate tremendous potential for IEM to enhance project workflows through practices especially in the area of lean management, Six Sigma methods, and advanced simulation techniques. These methods, when merged with digital tools such as Internet of Things (IoT), real time data analytics and Building Information modeling (BIM), can potentially reduce the project cycles and decrease waste. Nevertheless, the research also indicates a lack of evidence in the long term empirical validation of these techniques since much of the data available comes from pilot projects or controlled environment. This paves the way to rethink how such practices could be deployed in large scale, real world infrastructure projects with very diverse conditions.

Improved Cost Control and Financial Oversight:

One such finding is the potential for advanced digital solutions in the potential to radically transform the practice of cost management. It is demonstrated that, the integration of 5D-BIM with these existing financial management methods like the Earned Value Management leads to increased accuracy in cost estimates and immediate budget performance insight. However, literature describes past obstacles to achieving these promising results. Forecasted and actual costs still do not match so therefore while technological advances provide more visibility and predictive power you still cannot consistently and effectively use them in different project contexts with different regulatory environments. This requires further refinement of these tools for them to better fit practical realities.

Optimized Resource Allocation through Quantitative Methods:

The outcomes of the work recommend that these sorts of quantitative optimization techniques, for example, genetic algorithms, ant colony optimization, and AI used guide predictive models, can provide enormous positive impacts in the field of resource allocation problems. These methods can be performed so as to dynamically balance the deployment of labor, materials, and equipment, in a responsive and efficient manner. However, practical evidence for these is still emergent despite good theoretical frameworks. Some of the purported benefits are cast as potential improvements for which more comprehensive, data-driven case studies are required to validate such approaches in operational settings.

Integration Barriers and Organizational Challenges:

While there appears to be considerable advantages to IEM practice, the review also brings out many barriers to integrating seamless IEM practice into traditional, civil engineering settings. The emergence of organizational inertia, entrenched hierarchical structures, resistance to change, amongst other things become main impediments. But on top of that, as well, legacy systems and technology infrastructures that are outdated make it harder to adopt new innovative digital tools. These challenges indicate that the technical merit of IEMs is well understood, but the practical implementation of the concept entails a radical change in the culture and management of the organization.

5.2 Contributions to the Field

This study advances the practice and theory of civil engineering management, and the contributions offered in this work are poised to change the way large scale projects are managed.

Development of an Integrated Theoretical Framework:

A major contribution lies in the formulation of a comprehensive framework (illustrated in Figure 2 below) for systematical process optimization, cost control and dynamic resource allocation under IEM. Then, this framework does not only synthesize different studies but also offers a structured model that unite the civil engineering practices with the industrial engineering practices. The framework integrates principles from lean management, systems theory and digital transformation to provide a new lens for understanding and managing the complexities of large scale projects.

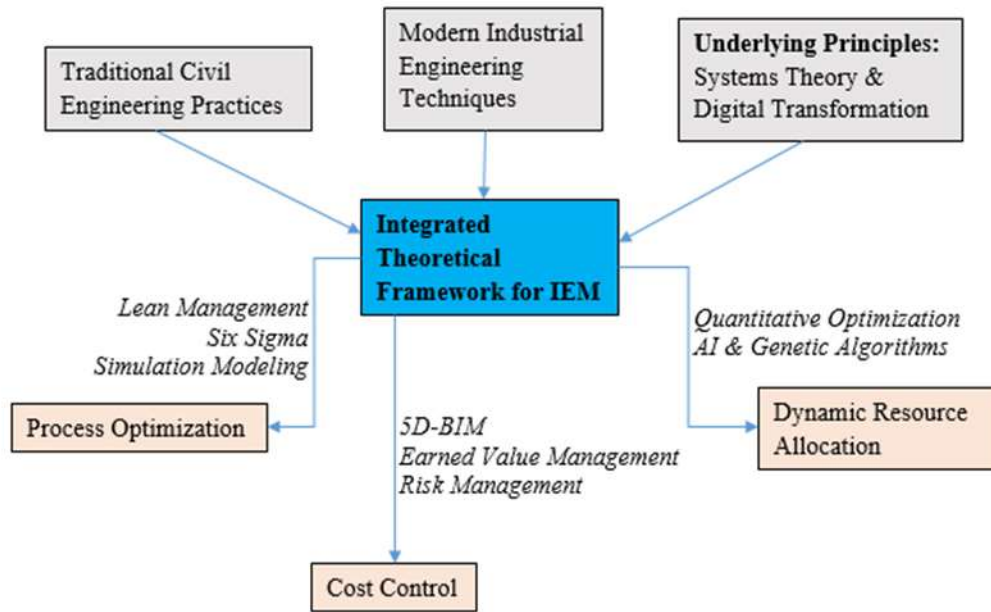


Figure 2: Integrated Theoretical Framework of Industrial Engineering Management (IEM)

Bridging Disciplinary Boundaries:

The study has a very significant interdisciplinary contribution in combining both the methodological rigor of industrial engineering and the practical issues in civil infrastructure development. The exchange between fields in these silos leads to cross-pollination of ideas which enriches the academic discourse, opening avenues for collaborative research. By so doing, it also undermines the traditional content of project management in civil engineering and offers new practices aimed at improving large scale projects efficiency and sustainability.

Empirical and Practical Implications:

The research while desk based aims to identify key performance indicators and areas for pilot testing more detailed empirical studies. The proposed framework represents a vital guide for practitioners by identifying actionable insights of how to integrate advanced digital tools with the currently well-developed management practices. The study for policymakers underline that there is strong need for supportive regulatory environment and strategic partnerships that can create appropriate conditions for the adoption of IEM practices to enable the translation of the technological advance as realization of real project performance improvements.

Identification of Research Gaps and Future Directions:

The study delineates several areas where further research is imperative in its critical examination of the literature. Specifically, these include the need for longitudinal field studies to validate the use of IEM practices in practice, the need to explore more deeply the human and cultural factors involved in technology adoption, and the integration of sustainability metrics into the traditional project management framework. Through this articulation of these gaps, the research contributes to widening the existing understanding of IEM in civil engineering, and it provides a robust agenda for future investigations to produce more resilient and adaptive project management strategy.

5.3 Limitations

However, there are several limitations to be critically acknowledged while the study offers significant insights:

- i. **Reliance on Secondary Data:** Although desk based approach is exhaustive, it depends on secondary data for which empirical validation is inherently limited. However, most of the evidence has come from theoretical models or pilot studies, and this evidence may not account for all of the complexities experienced in the live project environment.
- ii. **Temporal Constraints and Technological Dynamism:** The development of digital technologies and data analytics has been very rapid; hence, some of the reviewed methodologies are likely to become obsolete in time. Due to the dynamic nature of IEM applications, constant research has to be done to mainly ensure that the proposed frameworks are still relevant and effective.
- iii. **Contextual Variability:** The review pays particular attention to projects in regions with well-established civil engineering practices (North America, Europe, and parts of Asia) which are also likely benefiting from more risk diversification and strong economic signals. The results may not be applicable in a universal sense due to this geographical bias.

5.4 Future Research Directions

To advance the field, future studies should consider the following research trajectories:

- i. **Empirical Field Studies:** The proposed IEM framework needs to be empirically tested through longitudinal and cross sectional studies in real world project domains. Such research should focus to quantify the effects that the planned integrated IEM practices would have on the cost savings, time efficiency, and overall project success.
- ii. **Exploration of Organizational and Cultural Dynamics:** Additional research should explore human factors that either promote or hinder the adoption of IEM techniques. Understanding change management processes, leadership strategies and workforce adaptability are indispensable to overcoming resistance to change in the institution.
- iii. **Integration of Emerging Technologies:** While future research can integrate emerging technologies such as digital twins, advanced AI models and higher capabilities for cybersecurity to improve IEM applications, it is also necessary to consider the potential side effects of the integration of such advanced technologies. These technologies will be invaluable to comparative studies that evaluate them across various types and regions of projects.
- iv. **Sustainability and Resilience Metrics:** Incorporating both environmental and social sustainability into the IEM framework is a promising direction for how sustainability and resilience metrics can be included. Future work should be aimed at formulating integrated models that bridge operational efficiency and sustainability objectives to improve civil infrastructure long-term resilience.
- v. **Comparative and Cross-Regional Analyses:** Finally, comparative and cross-regional analysis of IEM implementation across various cultural, regulatory, and economic contexts is necessary. This could help with the development of more context specific, adaptable, universally applicable frameworks.

References

- Abbas, N. N. and Burhan, A. M., 2023. Evaluation of the current status of the cost control processes in Iraqi construction projects. *Journal of Engineering* [online], 29 (1), 128–144. Available from: <https://doi.org/10.31026/j.eng.2023.01.08>.
- Abishek, S., Prabakaran, P. A., Bharath, A. A. and Vaardhini, S., 2023. OPTIMIZING RESOURCE ALLOCATION AND SCHEDULING IN CONSTRUCTION PROJECTS USING AI & OPTIMIZATION ALGORITHMS. *INTERANTIONAL JOURNAL OF SCIENTIFIC RESEARCH IN ENGINEERING AND MANAGEMENT* [online], 07 (12), 1–10. Available from: <https://doi.org/10.55041/ijrsrem27863>.
- Adegbite, B. M., 2024. Applying lean principles to eliminate project waste, maximize value, cut superfluous steps, reduce rework and focus on customer centricity. *International Journal of Innovative Science and Research Technology (IJISRT)* [online], 1760–1768. Available from: <https://doi.org/10.38124/ijisrt/ijisrt24feb1682>.
- Afana, O., Zubaidi, R. A., Dabous, S. A. and Ibrahim, F., 2024. Categories and Factors of cost overrun in Construction Projects: A Systematic review. *Engineering Technology & Applied Science Research* [online], 14 (6), 18330–18347. Available from: <https://doi.org/10.48084/etasr.9006>.
- Agostini, L. and Filippini, R., 2019. Organizational and managerial challenges in the path toward Industry 4.0. *European Journal of Innovation Management* [online], 22 (3), 406–421. Available from: <https://doi.org/10.1108/ejim-02-2018-0030>.
- Ahiaga-Dagbui, D. D., Love, P. E. D., Smith, S. D. and Ackermann, F., 2017. Toward a Systemic View to Cost Overrun Causation in Infrastructure Projects: A Review and Implications for research. *Project Management Journal* [online], 48 (2), 88–98. Available from: <https://doi.org/10.1177/875697281704800207>.
- Akpe, N. A. T., Nuan, N. S. I., Solanke, N. B. and Iriogbe, N. H. O., 2024. Development and implementation of cost control strategies in oil and gas engineering projects. *Global Journal of Advanced Research and Reviews* [online], 2 (1), 001–022. Available from: <https://doi.org/10.58175/gjarr.2024.2.1.0028>.
- Alencar, A. C. P., 2024. MAPEAMENTO DE PROCESSOS NA ENGENHARIA CIVIL: OTIMIZAÇÃO DO MONITORAMENTO e EXECUÇÃO DE PROJETOS. *Revista Fisio&Terapia*. [online], 13–14. Available from: <https://doi.org/10.69849/revistaf/ar10202410212213>.
- Aljanabi, N. M., 2023. Navigating the Landscape: A comprehensive bibliometric analysis of Decision-Making research in civil engineering. *Mesopotamian Journal of Civil Engineering*. [online], 2023. Available from: <https://doi.org/10.58496/mjce/2023/005>.
- Amjad, M. H. H., Shovon, M. S. S. and Hasan, A. S. M. M., 2024. Analyzing Lean Six Sigma Practices In Engineering Project Management: A Comparative Analysis. *Innovatech Engineering Journal* [online], 1 (01), 245–255. Available from: <https://doi.org/10.70937/itej.v1i01.27>.
- Ashkanani, S. and Franzoi, R., 2022a. Gaps in megaproject management system literature: a systematic overview. *Engineering Construction & Architectural Management* [online], 30 (3), 1300–1318. Available from: <https://doi.org/10.1108/ecam-12-2021-1113>.
- Ashkanani, S. and Franzoi, R., 2022b. An overview on megaproject management systems. *Management Matters* [online], 19 (2), 129–148. Available from: <https://doi.org/10.1108/manm-01-2022-0006>.

- Ashtari, M. A., Ansari, R., Hassannayebi, E. and Jeong, J., 2022. Cost overrun risk assessment and prediction in construction Projects: A Bayesian Network Classifier approach. *Buildings* [online], 12 (10), 1660. Available from: <https://doi.org/10.3390/buildings12101660>.
- Aung, N. T., Liana, S. R., Htet, A. and Bhaumik, N. A., 2023. Using machine learning to predict cost overruns in construction projects. *Journal of Technology Innovations and Energy* [online], 2 (2), 1–7. Available from: <https://doi.org/10.56556/jtie.v2i2.511>.
- Baca, J., Carruth, D., Davis, E. and Waddell, D., 2018. Merging the cultures of design and Engineering: A case study. In: *Lecture notes in computer science* [online]. 628–641. Available from: https://doi.org/10.1007/978-3-319-91797-9_44.
- Benni, R., Akshata, G. K. and Neelamma, C. T., 2024. Meta-Heuristic Approaches to NP-Hard Resource Allocation in Civil Engineering: DE vs GA. 2024 *International Conference on Intelligent Systems and Advanced Applications (ICISAA)* [online], 1–7. Available from: <https://doi.org/10.1109/icisaa62385.2024.10829356>.
- Berawi, M. A., Miraj, P. and Sari, M., 2024. Advancing Construction Practices: Innovations, efficiency, and safety in the digital era. *CSID Journal of Infrastructure Development* [online], 7 (2), 225–227. Available from: <https://doi.org/10.7454/jid.v7.i2.1162>.
- Buczacki, A., Gładysz, B. and Timler, D., 2019. Industrial engineering for healthcare management – example lean management and ICT tools. *Studies in Logic Grammar and Rhetoric* [online], 60 (1), 19–32. Available from: <https://doi.org/10.2478/slgr-2019-0042>.
- Canesi, R. and Gallo, B., 2023. Risk assessment in sustainable infrastructure development projects: a tool for mitigating cost overruns. *Land* [online], 13 (1), 41. Available from: <https://doi.org/10.3390/land13010041>.
- Das, N. T., 2024. Productivity optimization techniques using industrial engineering tools: A review. *International Journal of Science and Research Archive* [online], 12 (1), 375–385. Available from: <https://doi.org/10.30574/ijrsra.2024.12.1.0820>.
- Delatte, N. J., 2017. Challenges of civil engineering megaprojects in North America. *Proceedings of the Institution of Civil Engineers - Management Procurement and Law* [online], 170 (4), 161–166. Available from: <https://doi.org/10.1680/jmapl.17.00012>.
- Demirdöğen, G., Diren, N. S., Aladağ, H. and Işık, Z., 2021. Lean Based Maturity Framework Integrating Value, BIM and Big Data Analytics: Evidence from AEC Industry. *Sustainability* [online], 13 (18), 10029. Available from: <https://doi.org/10.3390/su131810029>.
- Deuse, J., West, N. and Syberg, M., 2022. Rediscovering scientific management. The evolution from industrial engineering to industrial data science. *International Journal of Production Management and Engineering* [online], 10 (1), 1–12. Available from: <https://doi.org/10.4995/ijpme.2022.16617>.
- Dey, P., 2010. Issues and challenges of managing projects in India: A case study. In: *Routledge eBooks* [online]. 163–179. Available from: <https://doi.org/10.4324/9780203840931-20>.
- Dutta, N. S. S., 2024. Lean manufacturing and process Optimization : enhancing efficiency in modern production. *International Journal of Scientific Research in Computer Science Engineering and Information Technology* [online], 10 (5), 265–273. Available from: <https://doi.org/10.32628/cseit241051024>.
- Eldin, A. M. S., Abdelalim, A. and Tantawy, M., 2024. Enhancing cost management in construction: The role of 5D Building Information Modeling (BIM). *Engineering Research Journal* [online], 183 (3), 226–251. Available from: <https://doi.org/10.21608/erj.2024.377303>.
- Elghaish, F., Hosseini, M. R., Talebi, S., Abrishami, S., Martek, I. and Kagioglou, M., 2020. Factors driving success of cost management practices in Integrated Project delivery (IPD). *Sustainability* [online], 12 (22), 9539. Available from: <https://doi.org/10.3390/su12229539>.
- Elmalky, A., Mohamed, S. and Eldash, K., 2024. Impact of adopting lean principles on construction waste in developing countries. *Deleted Journal* [online], 53 (2), 82–93. Available from: <https://doi.org/10.21608/erjsh.2023.250653.1251>.
- Elserougy, M., Khodeir, L. M. and Fathy, F., 2024. Practices and techniques for construction projects cost control- a critical review. *HBRC Journal* [online], 20 (1), 525–552. Available from: <https://doi.org/10.1080/16874048.2024.2337060>.
- Ghannam, O., Ojiako, U. and Dweiri, F., 2024. Exploring Barriers to Implementing Industry 4.0 in Engineering Management: A Theoretical investigation. 2022 *Advances in Science and Engineering Technology International Conferences (ASET)* [online], 1–7. Available from: <https://doi.org/10.1109/aset60340.2024.10708743>.
- Goda, D. R., Vadiyala, V. R., Yerram, S. R. and Mallipeddi, S. R., 2023. Dynamic Programming Approaches for Resource Allocation in Project Scheduling: Maximizing Efficiency under Time and Budget Constraints. *ABC Journal of Advanced Research* [online], 12 (1), 1–16. Available from: <https://doi.org/10.18034/abcjar.v12i1.722>.
- Gunduz, M. and Maki, O. L., 2018. ASSESSING THE RISK PERCEPTION OF COST OVERRUN THROUGH IMPORTANCE RATING. *Technological and Economic Development of Economy* [online], 24 (5), 1829–1844. Available from: <https://doi.org/10.3846/20294913.2017.1321053>.
- Gupta, A., 2020. Resource Allocation with Primavera-P6 Software. *International Journal for Research in Applied Science and Engineering Technology* [online], 8 (10), 406–409. Available from: <https://doi.org/10.22214/ijraset.2020.31903>.

- Hagström, M. H., Bergsjö, D. and Wahrén, H., 2023. BARRIERS FROM a SOCIO-TECHNICAL PERSPECTIVE TO IMPLEMENT DIGITALISATION IN INDUSTRIAL ENGINEERING PROCESSES – A LITERATURE REVIEW. *Proceedings of the Design Society* [online], 3, 737–746. Available from: <https://doi.org/10.1017/pds.2023.74>.
- He, M., 2022. Innovative Management Approaches in Construction Engineering: Case Studies from 2022. *International Journal of Engineering and Innovation*. [online], 1 (1), 1–13. Available from: <https://doi.org/10.70088/cn25qp17>.
- Htet, A., Liana, S. R., Aung, T. and Bhaumik, A., 2023. Engineering Management: A comprehensive review of challenges, trends, and best practices. *Journal of Engineering Education and Pedagogy* [online], 1 (1), 1–7. Available from: <https://doi.org/10.56855/jeep.v1i1.262>.
- Hussein, A. R. and Moradina, S. F., 2023. Mitigating time and cost overruns in construction projects: A questionnaire study on integrating earned value management and risk management. *Journal of Studies in Science and Engineering* [online], 3 (2), 37–51. Available from: <https://doi.org/10.53898/josse2023323>.
- Hwang, B.-G., Shan, M., Zhu, L. and Lim, W.-C., 2018. Cost control in megaprojects: efficacy, tools and techniques, key knowledge areas and project comparisons. *International Journal of Construction Management* [online], 20 (5), 437–449. Available from: <https://doi.org/10.1080/15623599.2018.1484976>.
- Ibekwe, N. K. I., Umoh, N. A. A., Nwokediegwu, N. Z. Q. S., Etukudoh, N. E. A., Ilojiana, N. V. I. and Adefemi, N. A., 2024. ENERGY EFFICIENCY IN INDUSTRIAL SECTORS: A REVIEW OF TECHNOLOGIES AND POLICY MEASURES. *Engineering Science & Technology Journal* [online], 5 (1), 169–184. Available from: <https://doi.org/10.51594/estj.v5i1.742>.
- Imran, F., Shahzad, K., Butt, A. A. and Kantola, J., 2022. Structural challenges to adopt digital transformation in industrial organizations: A multiple case study. *AHFE International* [online]. Available from: <https://doi.org/10.54941/ahfe1002231>.
- Joglekar, N. R., Davies, J. and Anderson, E. G., 2016. The role of industry studies and public policies in production and operations management. *Production and Operations Management* [online], 25 (12), 1977–2001. Available from: <https://doi.org/10.1111/poms.12640>.
- Jonkers, R. K. and Shahroudi, K. E., 2020. Complexity, systems thinking and an integrated systems engineering and project management model. *INCOSE International Symposium* [online], 30 (1), 546–560. Available from: <https://doi.org/10.1002/j.2334-5837.2020.00739.x>.
- Kábele, P. and Edl, M., 2019. Increasing the efficiency of the production process due to using methods of industrial engineering. In: *Lecture notes in mechanical engineering* [online]. 126–137. Available from: https://doi.org/10.1007/978-3-030-22365-6_13.
- Karimidorabati, S., Haas, C. T. and Gray, J., 2016. Evaluation of automation levels for construction change management. *Engineering Construction & Architectural Management* [online], 23 (5), 554–570. Available from: <https://doi.org/10.1108/ecam-01-2015-0013>.
- Khan, M. N., Neaimi, A. K. A., Qamzi, A. A., Yusaf, S. A., Shimizu, Y., Asghar, A. and Menchaca, T. F., 2018. *Faster and Profitable Production Optimization Decisions through Workflow Automation and Business Process Management - A Unique Concept* [online]. Abu Dhabi International Petroleum Exhibition & Conference, Abu Dhabi, UAE, November 2018. Available from: <https://doi.org/10.2118/193343-ms>.
- Kozlov, R. N. and Peshkov, A. V., 2023. Integration of lean management and BIM technologies for effective project management and production processes at a construction stage. *Izvestiya Vuzov Investitsii Stroitelstvo Nedvizhimost* [online], 13 (2), 271–284. Available from: <https://doi.org/10.21285/2227-2917-2023-2-271-284>.
- Kravtsov, K., Kurashkin, S., Tynchenko, Y., Kukartsev, A. and Volneykina, E., 2024. Optimal resource allocation strategies in engineering projects using modern algorithms. *2022 International Conference on Decision Aid Sciences and Applications (DASA)* [online], 1–5. Available from: <https://doi.org/10.1109/dasa63652.2024.10836367>.
- Liao, Y., Loures, E. R., Deschamps, F., Brezinski, G. and Venâncio, A., 2018. The impact of the fourth industrial revolution: a cross-country/region comparison. *Production* [online], 28 (0). Available from: <https://doi.org/10.1590/0103-6513.20180061>.
- Lixiang, C., 2022. Research on civil engineering management and engineering cost control. *The Frontiers of Society Science and Technology* [online], 4 (1). Available from: <https://doi.org/10.25236/fsst.2022.040109>.
- Mabelo, P. B. and Sunjka, B. P., 2017. APPLICATION OF SYSTEMS ENGINEERING CONCEPTS TO ENHANCE PROJECT LIFECYCLE METHODOLOGIES. *The South African Journal of Industrial Engineering* [online], 28 (3). Available from: <https://doi.org/10.7166/28-3-1838>.
- Mangaroo-Pillay, M. and Roopa, M., 2021. BEYOND THE INDUSTRIAL ENGINEERING FRONTIER: a FEW STEPS IN HISTORY AND a GIANT LEAP INTO THE FUTURE. *The South African Journal of Industrial Engineering* [online], 32 (3). Available from: <https://doi.org/10.7166/32-3-2607>.
- Maradzano, I., Matope, S. and Dondofema, R. A., 2019. APPLICATION OF LEAN PRINCIPLES IN THE SOUTH AFRICAN CONSTRUCTION INDUSTRY. *The South African Journal of Industrial Engineering* [online], 30 (3). Available from: <https://doi.org/10.7166/30-3-2240>.
- Muralidhar, P., 2018. Analysis on improving operational efficiency of construction project site. *Independent Journal of Management & Production* [online], 9 (3), 827–839. Available from: <https://doi.org/10.14807/ijmp.v9i3.686>.

- Nahid, O. F., Rahmatullah, R., Al-Arafat, M., Kabir, M. E. and Dasgupta, A., 2024. RISK MITIGATION STRATEGIES IN LARGE SCALE INFRASTRUCTURE PROJECT:A PROJECT MANAGEMENT PERSPECTIVE. *Non Human Journal*. [online], 1 (01), 21–37. Available from: <https://doi.org/10.70008/jeser.v1i01.38>.
- Nguyen, P. and Akhavian, R., 2019. Synergistic effect of integrated project delivery, lean construction, and building information modeling on project performance measures: A quantitative and Qualitative analysis. *Advances in Civil Engineering* [online], 2019 (1). Available from: <https://doi.org/10.1155/2019/1267048>.
- Nounou, A., 2018. Developing a lean-based holistic framework for studying industrial systems. *Production Planning & Control* [online], 29 (13), 1096–1111. Available from: <https://doi.org/10.1080/09537287.2018.1517422>.
- Nsimbe, A. and Di, J., 2024. The impact of building information modeling technology on cost management of civil engineering projects: A case study of the Mombasa Port Area Development Project. *Buildings* [online], 14 (4), 1175. Available from: <https://doi.org/10.3390/buildings14041175>.
- Nwulu, N. E. O., Elele, N. T. Y., Omomo, N. K. O., Akano, N. O. A. and Erhueh, N. O. V., 2023. The importance of interdisciplinary collaboration for successful engineering project completions: A strategic framework. *World Journal of Engineering and Technology Research* [online], 2 (3), 001–016. Available from: <https://doi.org/10.53346/wjetr.2023.2.3.0048>.
- Olu-Lawal, N. K. A., Ekemezie, N. I. O. and Usiagu, N. G. S., 2024. Lean manufacturing in industrial engineering: A USA and African review. *GSC Advanced Research and Reviews* [online], 18 (2), 225–233. Available from: <https://doi.org/10.30574/gscarr.2024.18.2.0059>.
- Pauna, T., Lampela, H., Aaltonen, K. and Kujala, J., 2021. Challenges for implementing collaborative practices in industrial engineering projects. *Project Leadership and Society* [online], 2, 100029. Available from: <https://doi.org/10.1016/j.plas.2021.100029>.
- Pitsis, A., Clegg, S., Freeder, D., Sankaran, S. and Burdon, S., 2018. Megaprojects redefined – complexity vs cost and social imperatives. *International Journal of Managing Projects in Business* [online], 11 (1), 7–34. Available from: <https://doi.org/10.1108/ijmpb-07-2017-0080>.
- Poswa, F., Adenuga, O. T. and Mpofo, K., 2022. Productivity improvement using simulated value stream mapping: A case study of the truck manufacturing industry. *Processes* [online], 10 (9), 1884. Available from: <https://doi.org/10.3390/pr10091884>.
- Radman, K., Jelodar, M. B., Lovreglio, R., Ghazizadeh, E. and Wilkinson, S., 2022. Digital technologies and data-driven delay management process for construction projects. *Frontiers in Built Environment* [online], 8. Available from: <https://doi.org/10.3389/fbuil.2022.1029586>.
- Raper, S. A. and Murray, S. L., 1997. *Engineering Management And Industrial Engineering: Six One Way, A Half Dozen The Other* [online]. Available from: <https://doi.org/10.18260/1-2--6543>.
- Rudolf, C. A. and Spinler, S., 2018. Key risks in the supply chain of large scale engineering and construction projects. *Supply Chain Management an International Journal* [online], 23 (4), 336–350. Available from: <https://doi.org/10.1108/scm-09-2017-0292>.
- Sader, S., Husti, I. and Daróczy, M., 2019. Industry 4.0 as a Key Enabler toward Successful Implementation of Total Quality Management Practices. *Periodica Polytechnica Social and Management Sciences* [online], 27 (2), 131–140. Available from: <https://doi.org/10.3311/ppso.12675>.
- Sankaran, B., O'Brien, W. J., Goodrum, P. M., Khwaja, N., Leite, F. L. and Johnson, J., 2016. Civil Integrated Management for Highway Infrastructure: case studies and lessons learned. *Transportation Research Record Journal of the Transportation Research Board* [online], 2573 (1), 10–17. Available from: <https://doi.org/10.3141/2573-02>.
- Sankaran, S., Freeder, D., Pitsis, A., Clegg, S., Drouin, N. and Caron, M.-A., 2020. Megaprojects. *Urban Studies* [online]. Available from: <https://doi.org/10.1093/obo/9780190922481-0032>.
- Sharma, G. V. S. S., Prasad, C. L. V. R. S. V. and Rao, M. S., 2020. Industrial engineering into healthcare – A comprehensive review. *International Journal of Healthcare Management* [online], 14 (4), 1288–1302. Available from: <https://doi.org/10.1080/20479700.2020.1757874>.
- Sharma, S. and Gandhi, P. J., 2017. Banish Waste from Civil Engineering Operations Applying Lean Thinking. *MOJ Civil Engineering* [online], 3 (4). Available from: <https://doi.org/10.15406/mojce.2017.03.00078>.
- Sing, M. C. P., Love, P. E. D., Edwards, D. J. and Liu, J., 2016. Dynamic modeling of workforce planning for infrastructure projects. *Journal of Management in Engineering* [online], 32 (6). Available from: [https://doi.org/10.1061/\(asce\)me.1943-5479.0000463](https://doi.org/10.1061/(asce)me.1943-5479.0000463).
- Sravanthi, J., Sobti, R., Semwal, A., Shravan, M., Al-Hilali, A. A. and Alazzam, M. B., 2023. *AI-Assisted Resource Allocation in Project Management* [online]. 3rd International Conference on Advance Computing and Innovative Technologies in Engineering (ICACITE). Available from: <https://doi.org/10.1109/icacite57410.2023.10182760>.
- Sreeram, T. and Thondiyath, A., 2015. Combining Lean and Six Sigma in the context of Systems Engineering design. *International Journal of Lean Six Sigma* [online], 6 (4), 290–312. Available from: <https://doi.org/10.1108/ijlss-07-2014-0022>.
- Sumi, S. S., 2024. Innovative paths to productivity: Advancing lean manufacturing in industrial engineering. *World Journal of Advanced Research and Reviews* [online], 22 (3), 176–184. Available from: <https://doi.org/10.30574/wjarr.2024.22.3.1685>.

- Suvvari, N. S. K. and Saxena, N. Dr. V. D., 2023. Effective risk Management Strategies for Large-Scale projects. *Innovative Research Thoughts* [online], 9 (1), 406–420. Available from: <https://doi.org/10.36676/irt.v9.i1.1477>.
- Taghaddos, M., Mousaei, A., Taghaddos, H., Hermann, U., Mohamed, Y. and AbouRizk, S., 2023. Optimized variable resource allocation framework for scheduling of fast-track industrial construction projects. *Automation in Construction* [online], 158, 105208. Available from: <https://doi.org/10.1016/j.autcon.2023.105208>.
- Terra, J. D. R., Berssaneti, F. T. and Quintanilha, J. A., 2021. Challenges and barriers to connecting World Class Manufacturing and continuous improvement processes to Industry 4.0 paradigms. *Engineering Management in Production and Services* [online], 13 (4), 115–130. Available from: <https://doi.org/10.2478/emj-2021-0035>.
- Tian, T., Jia, N. S., Lin, N. J., Huang, N. Z., Wang, N. K. O. and Tang, N. Y., 2024. Enhancing Industrial Management through AI Integration: A Comprehensive Review of Risk Assessment, Machine Learning Applications, and Data-Driven Strategies. *Economics & Management Information* [online], 1–18. Available from: <https://doi.org/10.62836/emi.v3i4.243>.
- Tshering, D., 2023. Risk management as a dynamic and continuous process in the life cycle of a typical major civil engineering project. *Bhutan Journal of Research and Development* [online], (2). Available from: <https://doi.org/10.17102/bjrd.rub.se2.043>.
- Tshidavhu, F. and Khatleli, N., 2020. An assessment of the causes of schedule and cost overruns in South African megaprojects: A case of the critical energy sector projects of Medupi and Kusile. *Acta Structilia* [online], 27 (1), 119–143. Available from: https://doi.org/10.18820/24150487/as27i1_5.
- Umar, N. M. O., Okwandu, N. A. C. and Akande, N. D. O., 2024. Innovations in project monitoring tools for Large-Scale Infrastructure projects. *International Journal of Management & Entrepreneurship Research* [online], 6 (7), 2275–2291. Available from: <https://doi.org/10.51594/ijmer.v6i7.1294>.
- Uriarte, A. G., Ng, A. H. C., Zuniga, E. R. and Moris, M. U., 2017. Improving the material flow of a manufacturing company via lean, simulation and optimization. *2021 IEEE International Conference on Industrial Engineering and Engineering Management (IEEM)* [online], 1245–1250. Available from: <https://doi.org/10.1109/icem.2017.8290092>.
- Vembu, N. R., Saluja, R., Trivedi, J. B., Singh, B. P., Tyagi, M. and Bhateja, R., 2024. *Strategic Integration of Engineering and Management: Navigating Complex Challenges for Organizational Success* [online]. 4th International Conference on Innovative Practices in Technology and Management (ICIPTM). Available from: <https://doi.org/10.1109/iciptm59628.2024.10563213>.
- Vernadat, F. B., Chan, F. T. S., Molina, A., Nof, S. Y. and Panetto, H., 2018. Information systems and knowledge management in industrial engineering: recent advances and new perspectives. *International Journal of Production Research* [online], 56 (8), 2707–2713. Available from: <https://doi.org/10.1080/00207543.2018.1454615>.
- Viles, E., Ormazábal, M. and Lleó, A., 2017. *Closing the gap between practice and research in industrial engineering* [online]. Lecture notes in management and industrial engineering. Available from: <https://doi.org/10.1007/978-3-319-58409-6>.
- Ward, E. J., 2020. Mega infrastructure and strategic risk mitigation: planning, management and outcomes. *Journal of Mega Infrastructure & Sustainable Development* [online], 2 (1), 5–31. Available from: <https://doi.org/10.1080/24724718.2022.2035553>.
- Weihao, H., 2024. Review of Cost Control Research in Prefabricated Construction under EPC Mode. *Advances in Research* [online], 25 (4), 412–420. Available from: <https://doi.org/10.9734/air/2024/v25i41120>.
- Whyte, J., 2016. The future of systems integration within civil infrastructure: A review and directions for research. *INCOSE International Symposium* [online], 26 (1), 1541–1555. Available from: <https://doi.org/10.1002/j.2334-5837.2016.00244.x>.
- Wu, C., Chen, D. and Huang, S., 2018. Complexity of construction mega infrastructure project. *Complexity* [online], 2018 (1). Available from: <https://doi.org/10.1155/2018/7382083>.
- Wu, X., Zhao, W., Ma, T. and Yang, Z., 2019. Improving the efficiency of highway construction project management using lean management. *Sustainability* [online], 11 (13), 3646. Available from: <https://doi.org/10.3390/su11133646>.
- Yuan, B., 2023. The Prospects of building Information Modeling (BIM) and intelligent construction in civil Engineering for digital transformation. *Academic Journal of Science and Technology* [online], 8 (1), 52–55. Available from: <https://doi.org/10.54097/ajst.v8i1.13987>.
- Zaher, M. A. and Eldakhly, N. M., 2023. An integrated framework for dynamic resource allocation in multi-project environment. *American Journal of Business and Operations Research* [online], 10 (1), 08–15. Available from: <https://doi.org/10.54216/ajbor.100101>.
- Zhan, X., 2024. Research on fine cost control of civil engineering works supported by building information modeling. *Applied Mathematics and Nonlinear Sciences* [online], 9 (1). Available from: <https://doi.org/10.2478/amns-2024-2516>.
- Zhang, C., Kim, J., Jeon, J., Xing, J., Ahn, C., Tang, P. and Cai, H., 2022. Toward Integrated Human-Machine Intelligence for Civil Engineering: an Interdisciplinary Perspective. *Computing in Civil Engineering* [online], 279–286. Available from: <https://doi.org/10.1061/9780784483893.035>.
